

Arafah Aid...

GENAI IN PROJECT MANAGEMENT


From Manual Chaos to AI-Assisted Clarity

A Live 60-Minute Session

WHAT IS GENERATIVE AI?

GenAI is a type of artificial intelligence that can create new content, including text, images, code, audio, video, and even 3D models.

- » Learns from massive amount of data.
- » Learns the underlying patterns and structures within the data.
- » Generates new content that follows similar patterns and styles to the data it was trained on.

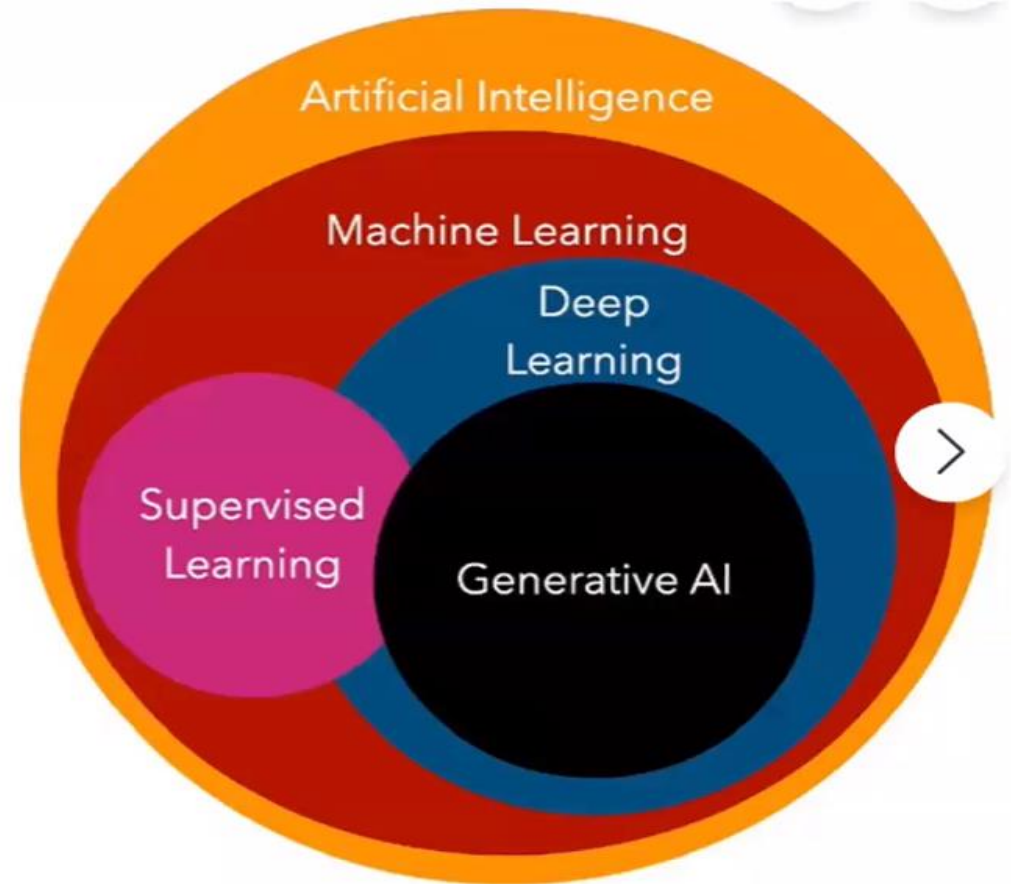

APPLICATIONS OF GENERATIVE AI

Content Creation

Financial Analysis

Coding Assistance

Image and Video Generation

Material Design

Product Design

Customer Support

Drug Discovery

Game Development

Hypothesis Generation

Document Summarization

Translation

Music Composition

Personalized Education

TRADITIONAL AI V/S GENERATIVE AI

Feature	Traditional AI	Generative AI
Primary goal	Analyze and interpret data	Create new data and content
Types of tasks	Image recognition, prediction, classification	Writing, Image Generation, Code Generation
Key strengths	Problem-solving within defined parameters	Creativity, originality, and synthesis of knowledge
Limitations	Difficulty generating truly new ideas	Potential for factual inaccuracy and bias
Example	Spam filters, facial recognition software, self-driving car navigation	ChatGPT, DALL-E 2 (image generation), AI-powered coding assistants

Exploring the Applications of Generative AI in Project Management



- **Project Planning**
 - Generative AI can create realistic and optimal project plans
 - Uses historical data, constraints, and objectives
- **Project Monitoring**
 - Generative AI can monitor progress and performance
 - Provides suggestions and alerts for corrective actions
- **Project Communication**
 - Generative AI can help communicate effectively with stakeholders
 - Generates reports tailored to the audience

What Just Took 45 Minutes Took 45 Seconds



The Manual Way

- Chase updates across Slack, email, and standups
- Manually reconcile who said what
- Format into a presentable report
- Rewrite it for a non-technical audience
- Send it — hope no one asks a hard question

~45 minutes, every week



The AI-Assisted Way

- Paste your raw standup notes
- AI triages what matters vs. noise
- Get a formatted stakeholder update instantly
- Tone already matches your audience
- Review, tweak, send

~45 seconds, live in front of you

Three Things That Change How You Manage Projects

Today, live — not theory, not slides. The actual prompts, the actual outputs.

01

Planning

Generate a project charter and RACI matrix in under a minute.

02

Communication

Turn messy meeting notes into an executive-ready update.

03

Monitoring

Catch schedule risk before it shows up in your status report.

DEMO 1 · PLANNING

Project Charter & RACI Generator in 60 Seconds

From a one-line project description to a usable charter, RACI matrix, and risk list.



Q

 Share
 


@ Plugins

Recents >

Workstream	PM	BA	Backend Dev 1	Backend Dev 2	Data Specialist	QA
Project Planning	A/R	C	I	I	I	I
Requirements Gathering	A	R	C	C	C	I
Solution Design	A	R	C	C	C	C
Salesforce Configuration	C	C	R	R	I	C
Data Mapping	C	R	C	I	A/R	C
Data Cleansing	I	C	I	I	A/R	C
Data Migration	C	C	I	I	A/R	C
API Integrations	C	C	A/R	R	C	C
Unit Testing	I	I	R	R	C	C

Auto Auto



DEMO 2 · COMMUNICATION

Messy Notes → Executive-Ready Update

The report you've lost evenings writing — generated in the time it takes to paste your notes.

Same Information. Completely Different Report.

RAW NOTES

rahul said backend API 70% done, blocked on vendor sandbox again (3rd time)

data migration - 40 records failed validation

client asked if we can move go-live from sept 15 to aug 30

lost 2 days last week, ravi was out sick

STAKEHOLDER UPDATE

Project is progressing with one active vendor-access blocker affecting the integration timeline. Data migration is on track pending a minor validation fix. Leadership input is needed on two items this week.

NEEDS FROM LEADERSHIP:

1. Escalate the vendor sandbox access ticket
2. Confirm whether Aug 30 go-live is feasible

FileEditViewHelp

CRM Migration Planning

Share

ChatGPT

New chatProjectsScheduledPluginsRecents

Status	Item	Current Position
On Track	UI Design	Client has approved the UI mockups, and development will begin as planned on Monday.
On Track	Core Development	Backend API integration is approximately 70% complete.
On Track	Team Engagement	Overall team morale remains positive despite increased workload pressures.
At Risk	Integration Testing Milestone	Integration testing is now expected to move from July 25 to approximately August 1–2 due to dependency and resource impacts.
At Risk	Data Migration	A test migration identified 40 validation failures that are being investigated, with character encoding currently the leading suspected cause.
At Risk	Budget	Project spend is currently \$52K of the \$80K budget. An additional \$8K software license renewal has been identified that was not included in the original budget.
At Risk	Resource Capacity	Recent unplanned absence highlighted limited backup coverage, and one team member is currently supporting multiple projects, creating capacity risk.
Blocked	Vendor Sandbox Access	API integration progress remains blocked by pending vendor sandbox access. The support request has been open since July 10 with no response despite repeated follow-up.
Decision Required	Go-Live Date	The client has requested moving the go-live date from September 15 to August 30. The feasibility and impact on scope, quality, and budget need to be assessed before any commitment is made.

thirumazhi

Message ChatGPT

Auto Auto

Search

16:16:3724-07-2026

DEMO 3 · MONITORING

Catching Delays Before They Happen

Cross-referencing a task tracker against meeting notes to predict risk two weeks out.

Beyond Prompting: What Is Agentic AI?

The next evolution — from answering questions to completing entire workflows on its own.

WHAT WE USED TODAY

Conversational AI

- You ask, it answers
- One prompt produces one output
- You chain each step yourself
- You review and re-prompt at every stage

WHERE IT'S HEADED

Agentic AI

- ✓ You set a goal, not a single instruction
- ✓ It plans the steps needed to get there
- ✓ It uses tools — code, data, files — to execute them
- ✓ It comes back when the task is done, or when it needs a decision from you

See It In Action: Julius AI

An agentic data analyst — give it one goal, and it plans and executes the rest.

YOU PROVIDE

A project budget or risk-register file (CSV/Excel), plus one goal:

"Analyze cost variance by workstream, flag the top 3 drivers of overrun, and forecast next month's spend."



That's it — one instruction, not five separate prompts.

THE AGENT DOES THE REST

- 1 Interprets the goal and plans the analysis
- 2 Writes and runs the code itself, no formulas needed
- 3 Builds the charts automatically
- 4 Explains the results in plain English
- 5 Flags anomalies you didn't even ask about

Search [Taskbar Icons: File Explorer, Edge, etc.] 16:29:36 24-07-2026 [System Tray Icons: Network, Volume, etc.]

Where This Hour Ends — And the Real Work Begins

These techniques work beautifully for one project. Here's what breaks down at scale:

1

Multi-Project Portfolios

Managing risk and reporting across 10+ concurrent projects, not just one.

2

Tool Integration

Connecting these workflows directly into Jira, Asana, or MS Project.

3

Your Own Prompt Library

Building reusable, tested prompts for your team's specific project types.

4

Governance & Accuracy

Checks and guardrails so AI-assisted PM data stays trustworthy at scale.

Certification in Generative AI in Project Management

Course Modules

DAY 1

Module 1
Introduction to Gen AI and Project Management

Duration: 1.5 hrs

Module 2
GenAI Tools & Techniques for Project Managers

Duration: 2 hrs

Module 3
Integrating GenAI into Project Management

Duration: 1.5 hrs

Module 4
Practical-Applications-and-Case-Case-Studies

Duration: 1 hr

Module 5
Initiation & Planning Phases with with GenAI

Duration: 1 hr

Course Modules

DAY 2

Module 6 GenAI for Project Risk, Cost & Quality Management

Duration: 1.5 hrs

Module 7 Monitoring, Risk Management & Future Trends and Innovations

Duration: 1 hr

Module 8 Practical Applications of GenAI in in Project Management and Tools Tools

Duration: 1 hr

Module 9 Generative AI Use Cases, Tools & Hands-On Demos for Project Management

Duration: 1 hr

Module 10 Generative AI Applications and Use Cases for Project Management

Duration: 1 hr

Module 11 Agentic AI for Project Managers Managers

Duration: 1.5 hrs

Learning Features

Global Case studies

Roleplay oriented learning

Gamification Assessments

Templates



Questions?

Let's build your AI-powered PM toolkit.

Certification in Generative AI in Project Management

Check with the Admin for further queries

