

PROJECT MANAGEMENT FOR NON-PROJECT MANAGERS

"Lead with Clarity, Deliver with Confidence"

29 – 30 JULY



Characters



- Red – The driver
- Blue – The Thinker
- Green – The Supporter
- Yellow – The Inspirer

Why Project Management Matters

- Setting clear and focused goals
- Managing resource effectively
- Minimizing risks and problems
- Ensuring project completion
- Maintaining quality of results
- Supporting communication and team collaboration
- Increase customer and stakeholder satisfaction
- Become a guide and future reference

Why Some People Can Manage Project Without Training?

- Years of practical experiences
- Natural Leadership & common sense
- Smaller project scale.
- Flexible & adaptive approach

But Here's Why Formal Knowledge Still Matters?

- Essential for large & complex projects
- Avoiding repeating mistake.
- Enable standardization & Audit
- Enhances credibility & professionalism
- Build organization teams

10 Reasons to Learn Project Management

WHY NON-PMS need PM

W – Work is now project-based

H – Heighten efficiency

Y – Your skills go cross-functional

N – New career opportunities

O – Operate better in project teams

N – No more stress & firefighting

P – Personal leadership growth


M – Suitable for All Professions

PM – Personal Mastery


Project, Program, Portfolio

Term	Definition
Project	A temporary endeavor undertaken to create a unique product, service, or result.
Program	A group of related projects managed in a coordinated way.
Portfolio	A collection of projects, programs, and other initiatives aligned to strategic objectives.

Organizational Strategy

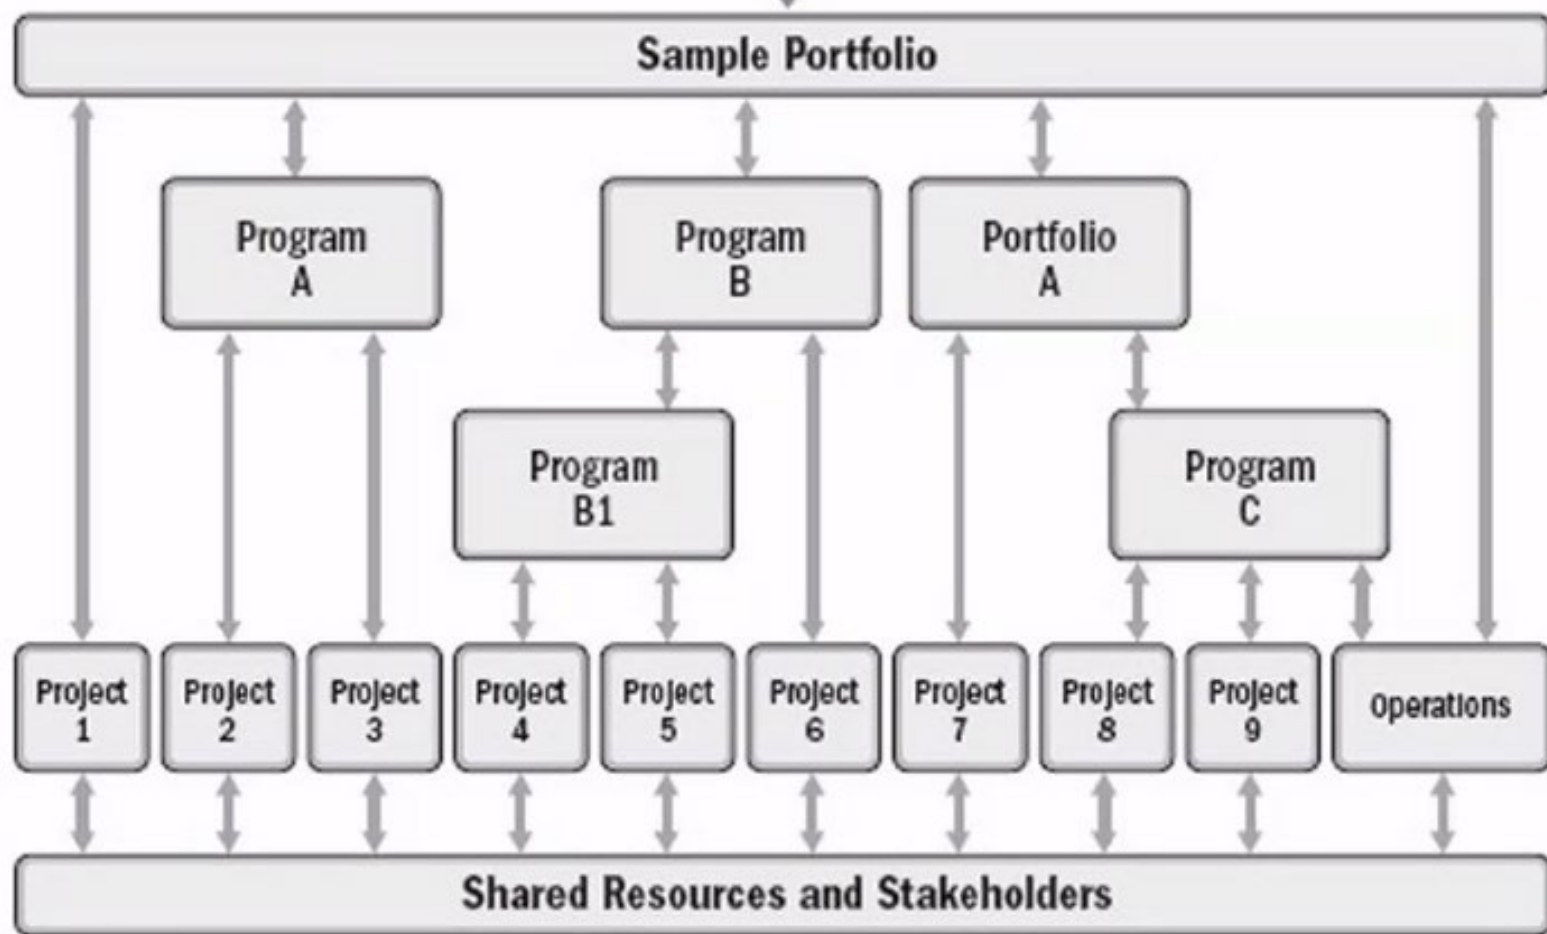


Aspect	Project	Program	Portfolio
Primary Focus	Output	Outcome	Strategic Alignment
Timeframe	Temporary	Longer-term	Ongoing
Risk Management	Project-level	Integrated across projects	Organizational-level
Sample Role	Project Manager	Program Manager	Portfolio Director

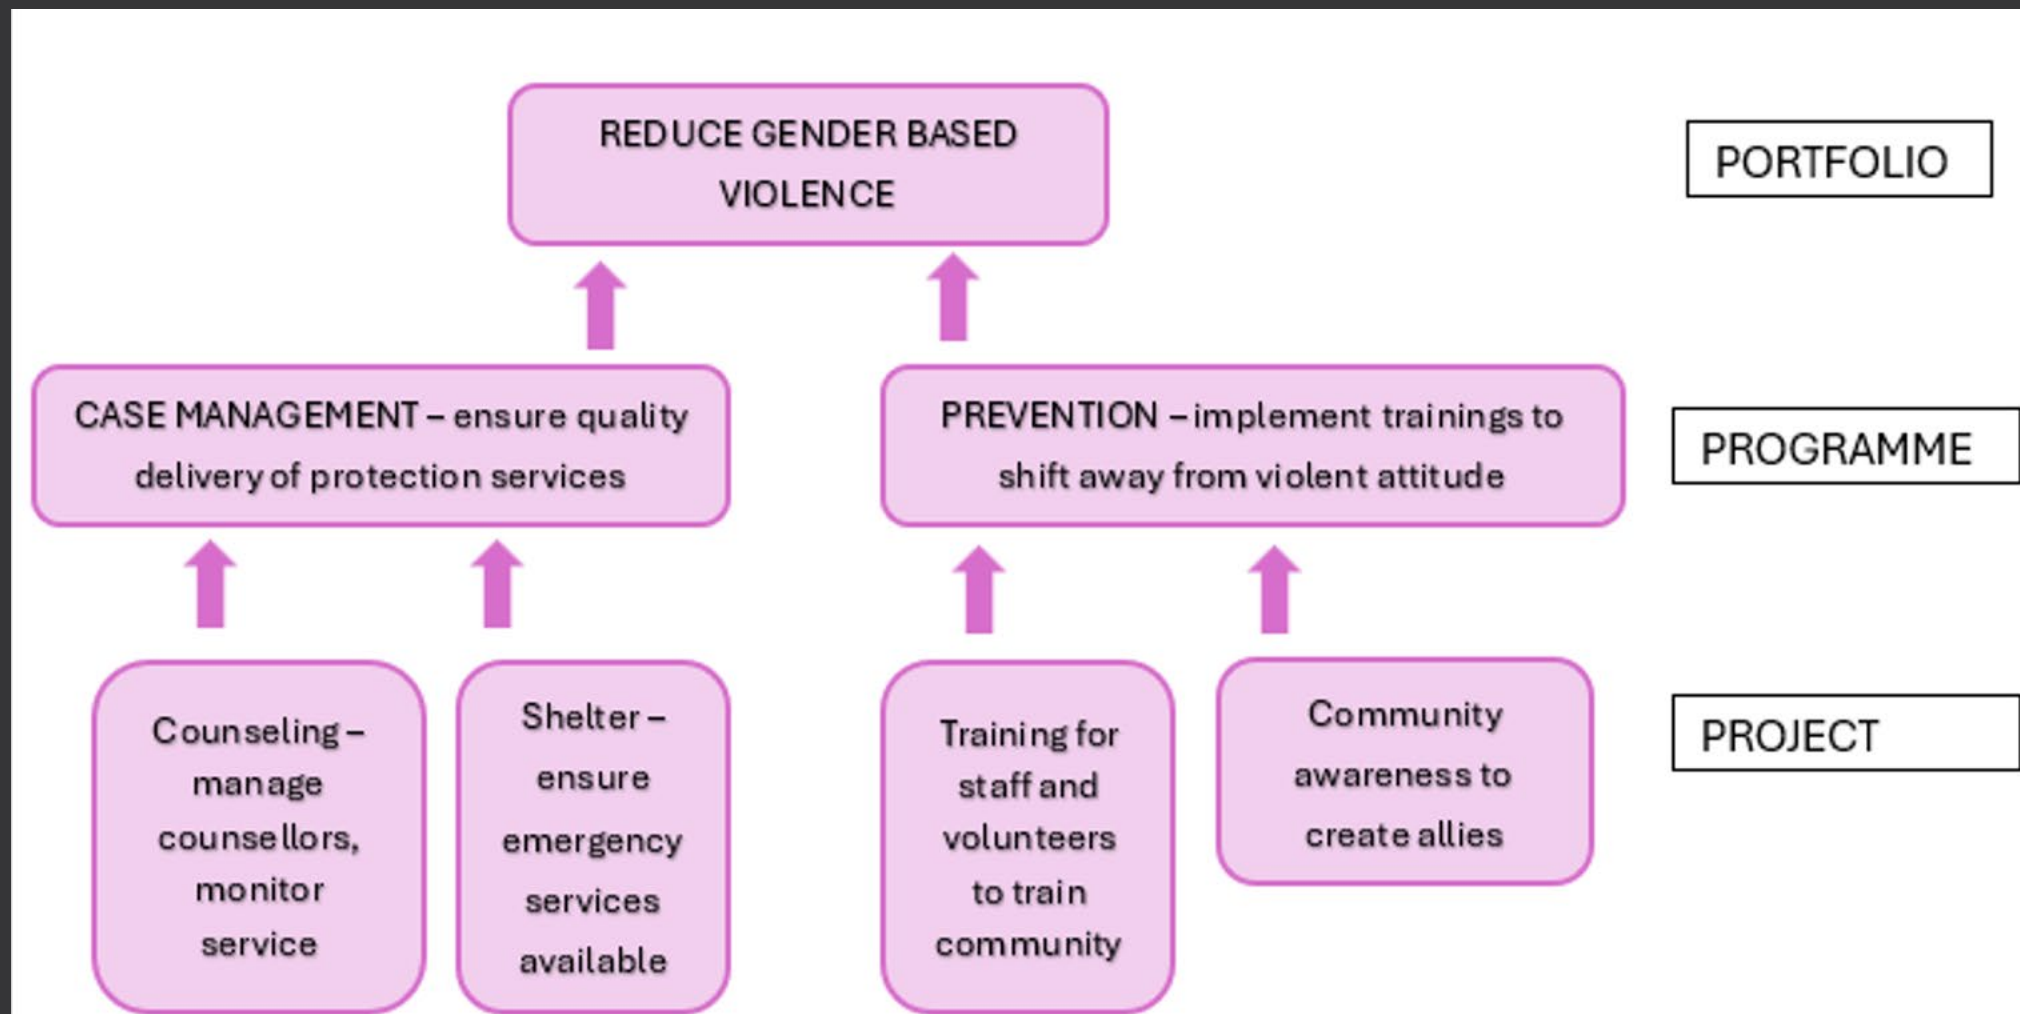

Pos Malaysia


- A **project** at Pos Malaysia could be the **installation of solar panels on a specific post office building** to reduce its energy consumption.
- A **program** at Pos Malaysia is their **Fleet Electrification Program**, which coordinates multiple projects like purchasing electric vehicles and building charging infrastructure to achieve their 2030 net-zero fleet target.
- A **portfolio** at Pos Malaysia encompasses **all of its strategic initiatives**, including programs like Digital Transformation and Sustainability, along with various individual projects and daily postal operations, all managed to achieve their long-term business goals like efficiency, growth, and environmental responsibility.

Project Life Cycle

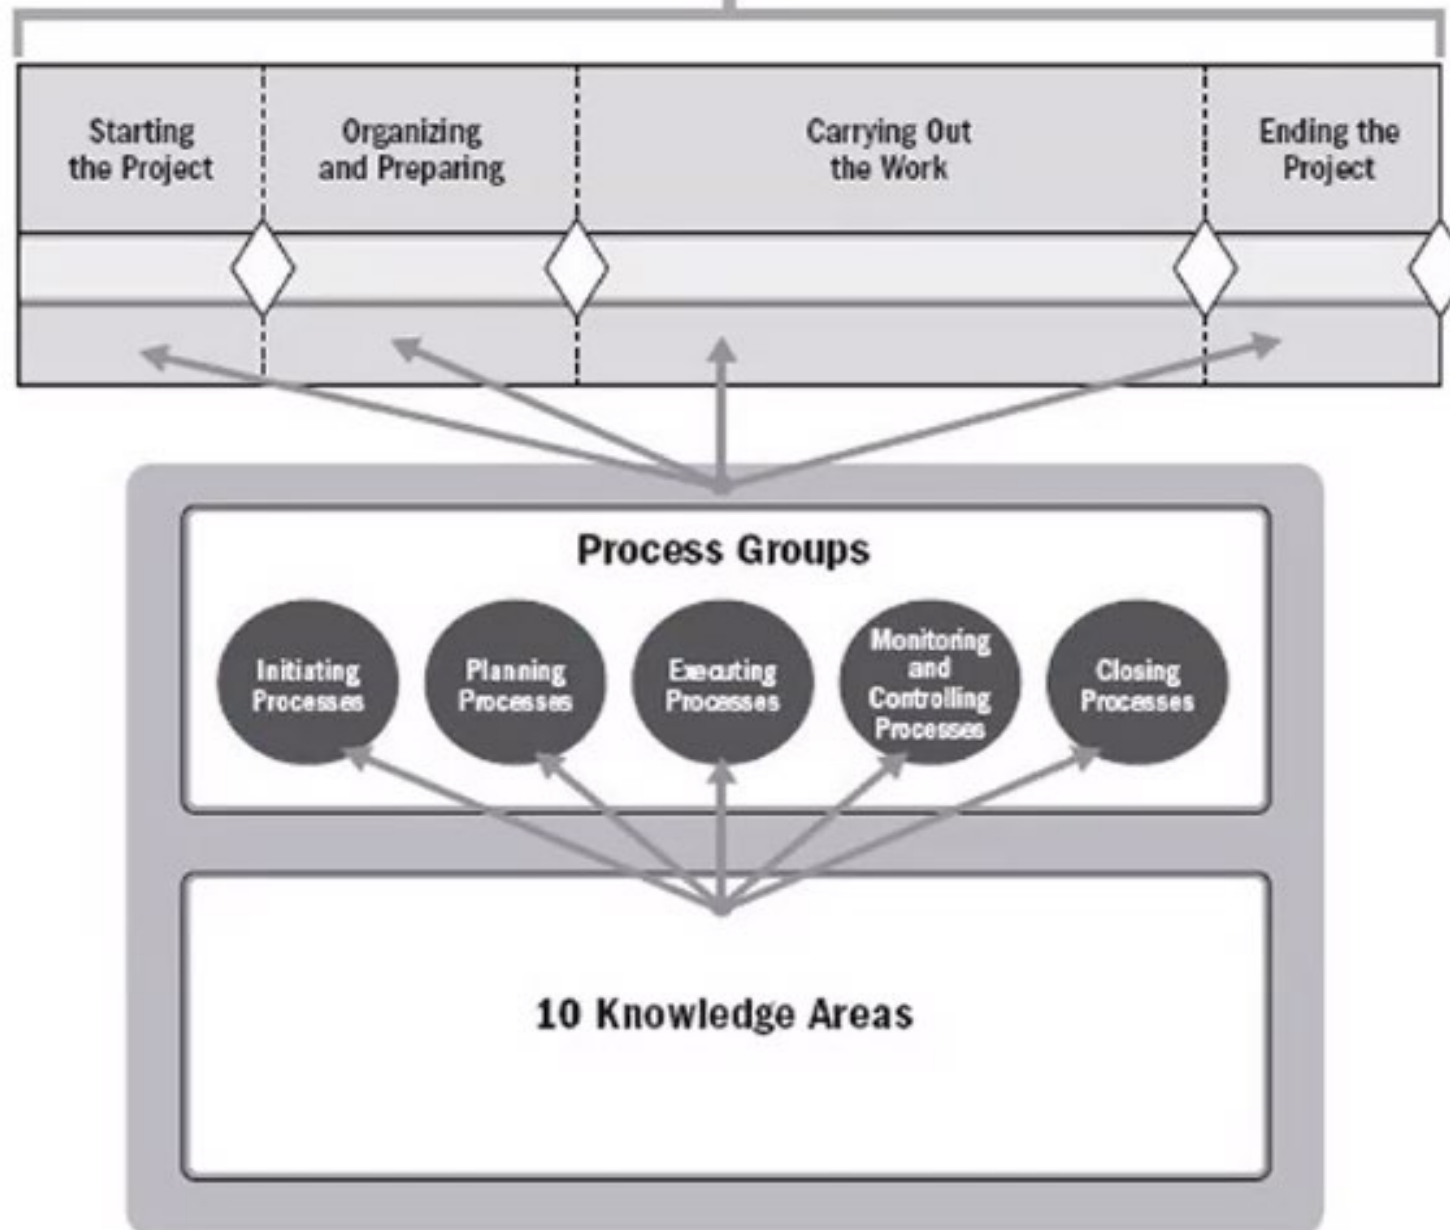

- **Project Life Cycle:** The steps a project takes from start to finish.
- **Process Groups:** What a project manager does at each step.
- **10 Knowledge Areas:** What a project manager needs to know about to do the job.

The Knowledge Areas To Organize Project Management

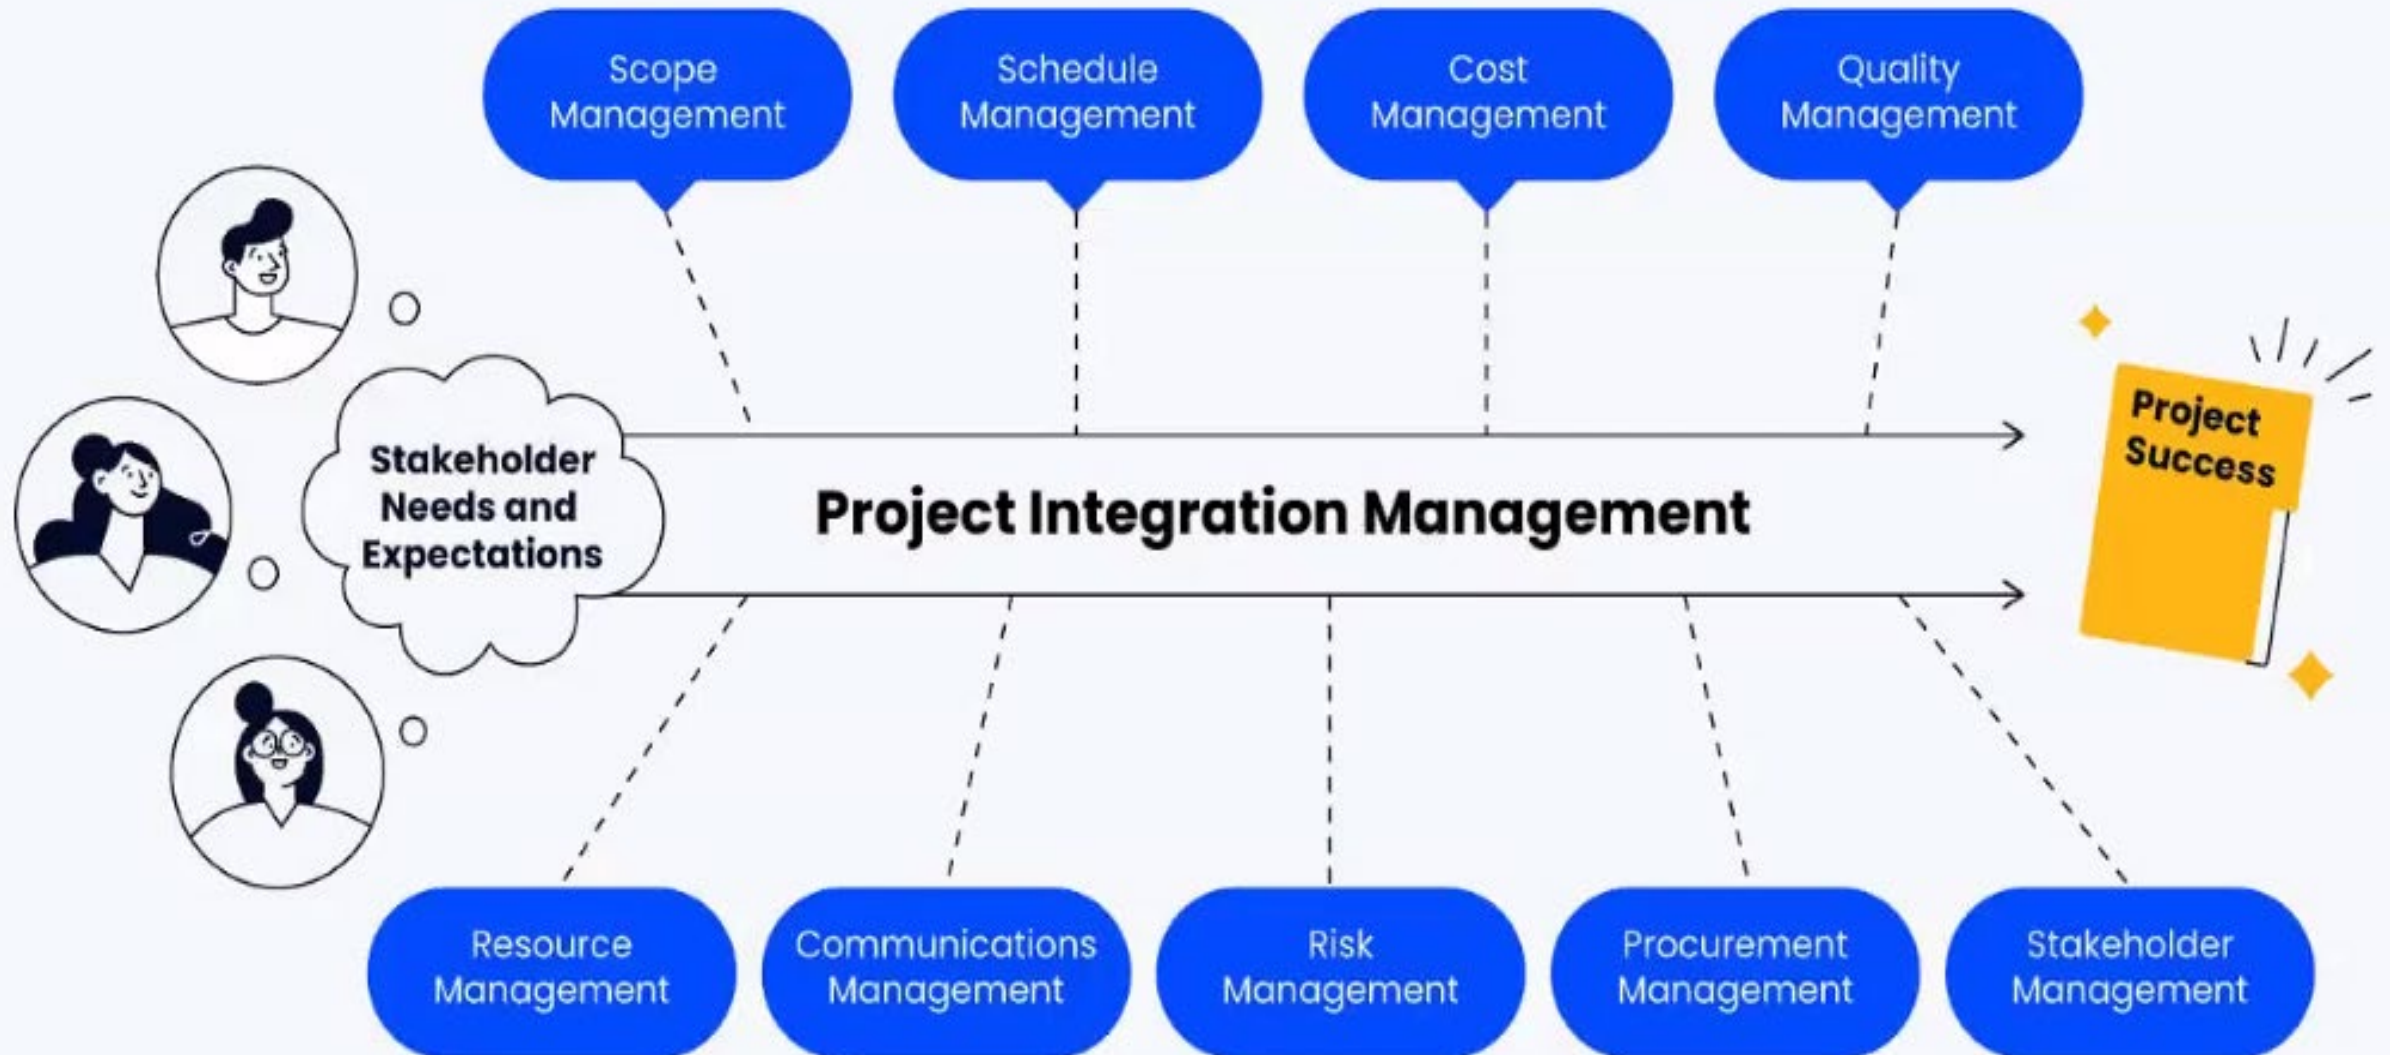

Good Project Manager

- Communication style - clarity, fairness, calmness
- Leadership style – directive, supportive, coaching, delegating.

SCQA (Situation, Complication, Question, Answer) – McKinsey Style

- **Situation:** What is the context?
- **Complication:** What is the issue or obstacle?
- **Question:** What do we need to solve?
- **Answer:** What action is recommended?

Example:

- **Situation:** Staff take a long time to complete reports.
- **Complication:** The data system is not centralized.
- **Question:** How can we reduce the time spent on reporting?
- **Answer:** Consolidate data using an automated dashboard.

Knowledge Area	Starting the Project(Initiating)	Organizing & Preparing(Planning)	Carrying Out the Work(Executing)	Monitoring & Controlling	Ending the Project(Closing)
1. Integration Management	✔ Project Charter	✔ Project Management Plan	✔ Direct & Manage Work	✔ Monitor & Control Work	✔ Close Project
2. Scope Management		✔ Collect Requirements Define Scope	✔ Validate Deliverables (implicitly)	✔ Control Scope	
3. Time/Schedule Management		✔ Define Activities Sequence Activities	✔ Execute Schedule Activities	✔ Control Schedule	
4. Cost Management		✔ Estimate CostsDetermine Budget	✔ Spend Budget as Planned	✔ Control Costs	
5. Quality Management		✔ Plan Quality	✔ Perform Quality Assurance	✔ Control Quality	
6. Resource Management		✔ Plan Resources	✔ Acquire & Manage Team	✔ Monitor Resources Usage	
7. Communication Management		✔ Plan Communication	✔ Manage Communications	✔ Monitor Communications	
8. Risk Management		✔ Identify & Analyse Risks Plan Responses	✔ Implement Risk Responses	✔ Monitor & Control Risks	
9. Procurement Management		✔ Plan Procurement	✔ Conduct Procurement	✔ Control Procurements	✔ Close Procurements
10. Stakeholder Management	✔ Identify Stakeholders	✔ Plan Stakeholder Engagement	✔ Manage Stakeholder Engagement	✔ Monitor Stakeholders	




PLANNING LIKE A PRO: SCHEDULE, COST AND SCOPE MANAGEMENT




Quadruple Constraints of Project Management



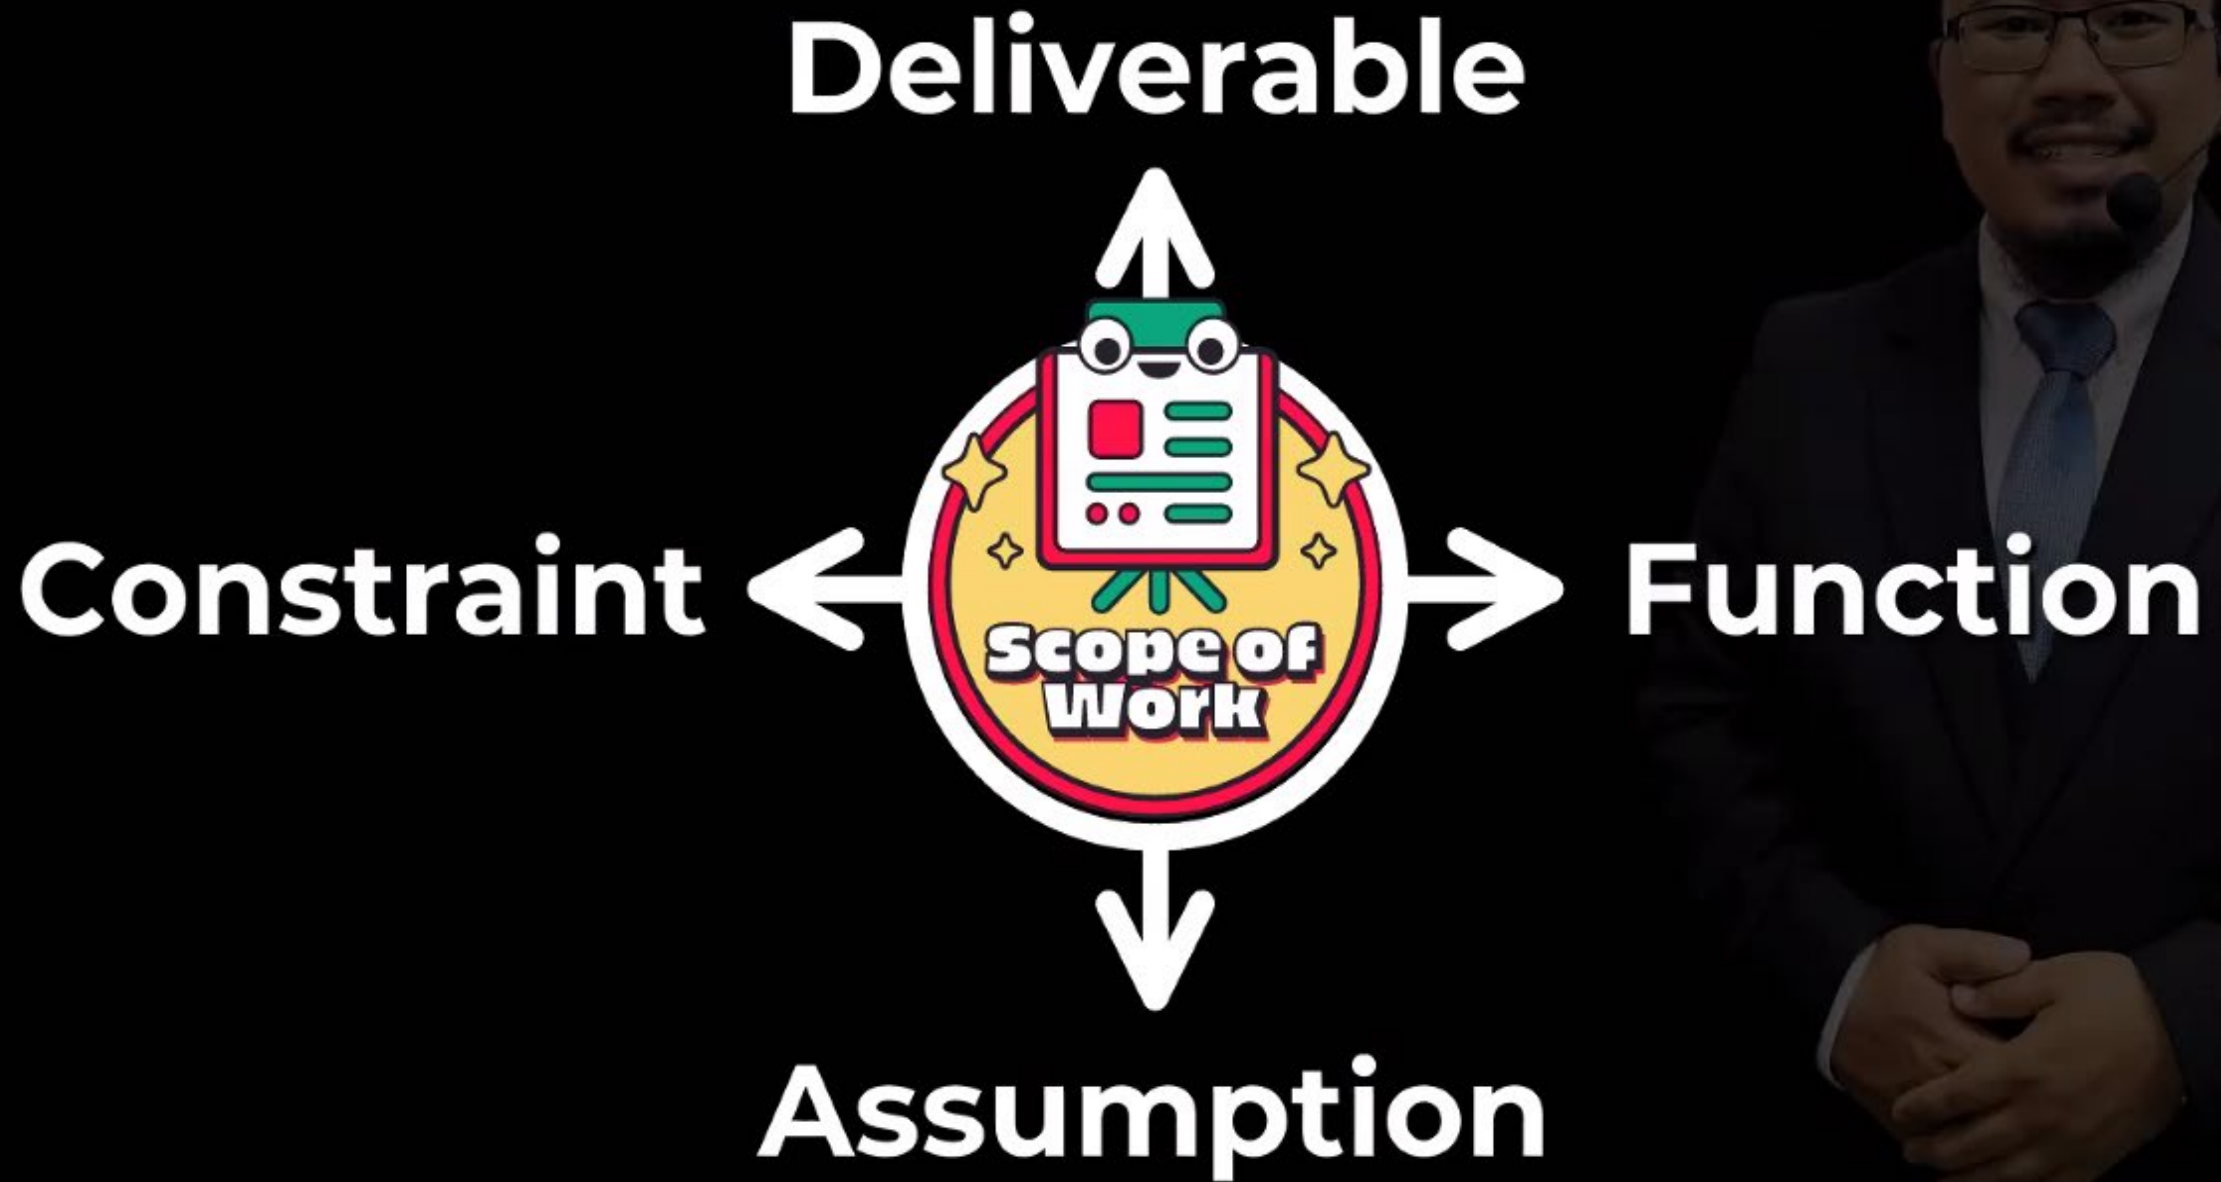



- **Scope Statement**
- **Work Breakdown Structure (WBS)**
- **Establish Change Control Process**
- **Engage stakeholders early**
- **Assess impact of new requests**
- **Use free tools: ClickUp, Trello, Notion**

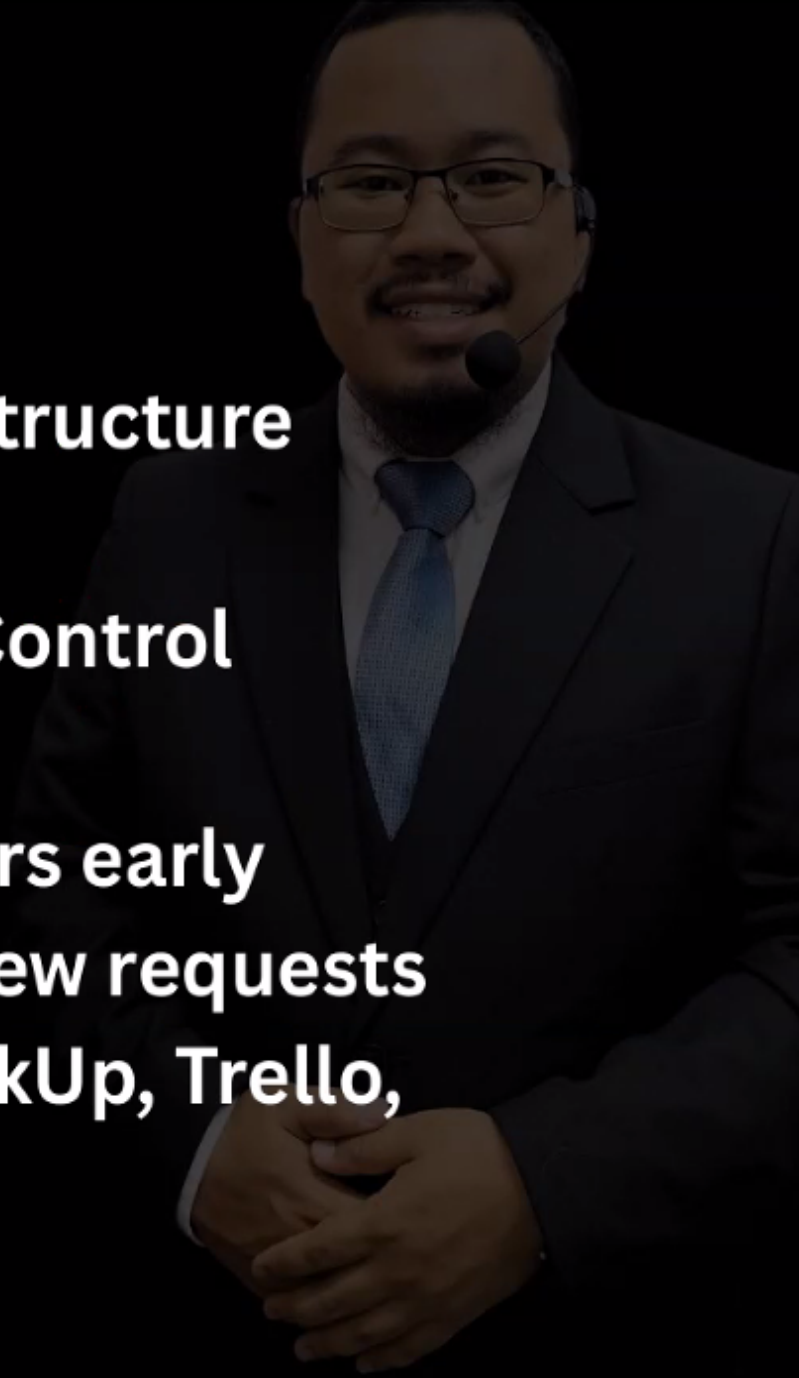

Construction of a House

Work	100%
Budget	\$215,500

Level 1

1. Internal

2. Foundation

3. External

Work	45.60%
Budget	\$86,000

Work	24.00%
Budget	\$46,000

Work	30.40%
Budget	\$83,500

1.1 Electrical

2.1 Excavate

3.1 Masonry Work

Electrical Contractor	
Work	11.80%
Budget	\$25,000

Labor Crew	
Work	18.20%
Budget	\$37,000

Masonry Contractor	
Work	16.20%
Budget	\$62,000

1.2 Plumbing

2.2 Steel Erection

3.2 Building Finishes

Plumbing Contractor	
Work	33.80%
Budget	\$61,000

G.C. Superintendent	
Work	5.8%
Budget	\$9,000


Painting Contractor	
Work	14.20%
Budget	\$21,500

Elements

Leg



- Use milestone planning
- Apply Critical Chain Method (buffering)
- Weekly monitoring: Gantt Chart/Burndown Chart
- Clarify roles using RACI Chart

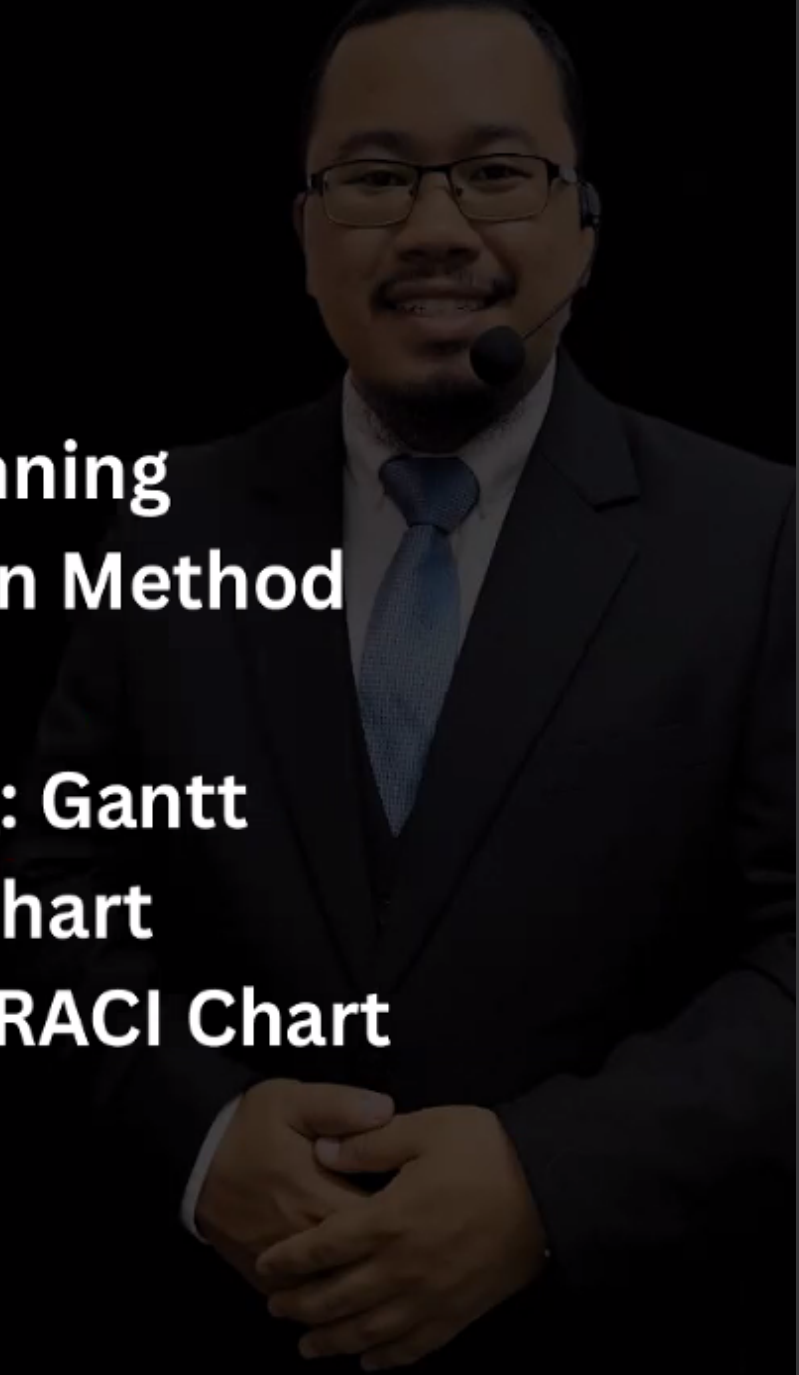

The RACI Matrix

Example & How to create one

I


TASK/ ACTIVITIES	PROJECT MANAGER	TEAM LEAD	DEVELOPER	TESTER	STAKEHOLDER
TASK 1	A	R	C	I	A
TASK 2	A	R	C	R	A
TASK 3	C	R	C	A	A
TASK 4	A	A	I	I	C
TASK 5	A	R	I	R	C



- **Set Cost Baseline and monitor regularly**
- **Use Earned Value Management (EVM)**
- **Include contingency reserve**
- **Renegotiate with vendors**



Figure 4

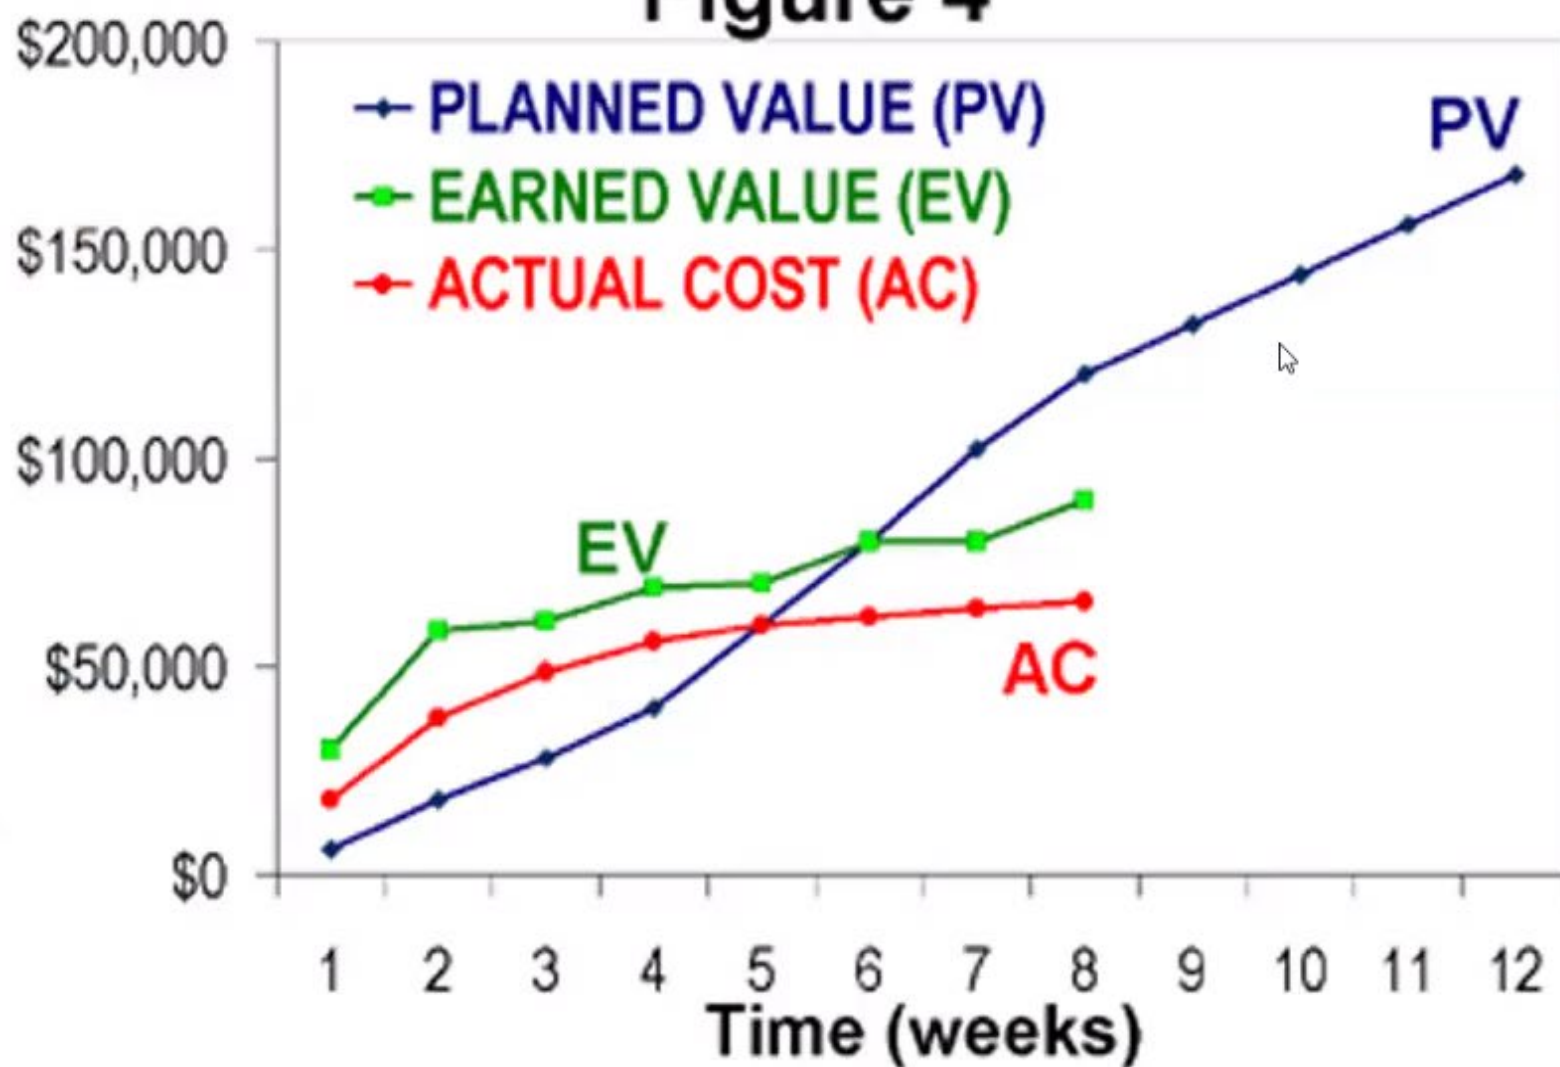

1. Cost Variance (CV) $CV = EV - AC$

- If CV is negative (–): Over budget
- If CV is positive (+): Under budget / Cost savings

2. Schedule Variance(SV) $SV = EV - PV$

- If SV is negative (–): Behind schedule
- If SV is positive (+): Ahead of schedule

3. Cost Performance Index (CPI) $CPI = EV \div AC$

- If < 1 : Not efficient
- If $= 1$: On budget
- If > 1 : More efficient

4. Schedule Performance Index (SPI) $SPI = EV \div PV$

- If < 1 : Behind schedule
- If $= 1$: On schedule
- If > 1 : Ahead of schedule

Step 3: Forecast Project Cost

➤ Estimate at Completion (EAC)

To estimate the final project cost:

$$EAC = BAC \div CPI$$

(BAC = Budget at Completion, i.e. the total project budget)

Example:

BAC = RM100,000, PV = RM60,000, EV = RM50,000, AC = RM55,000

Calculations:

- $CV = EV - AC = 50,000 - 55,000 = -5,000 \rightarrow$ Over budget
- $SV = EV - PV = 50,000 - 60,000 = -10,000 \rightarrow$ Behind schedule
- $CPI = 50,000 \div 55,000 = 0.91$
- $SPI = 50,000 \div 60,000 = 0.83$
- $EAC = 100,000 \div 0.91 = \text{RM}109,890$ (estimated final cost)

Conclusion:

“EVM is not just about budgeting, it reflects the true health of the project.”

Use EVM regularly (weekly/monthly) to monitor your project's performance systematically and take corrective actions if needed.



STAKEHOLDER, COMMUNICATION, RESOURCE AND PROCUREMENT MANAGAMENT



DMY Khairulanwar Misnan



Muslim Professional Helpers Center

Challenge

- Tools: Issue log, escalation path
- Use assertive communication
- Set mutual expectations via charter
- Communication plan
- Trains on teams
- Two-way communication
- RACI chart
- Team Charter
- Motivation sessions
- Procurement Plan
- Multi-vendor strategy
- Vendor audit & KPI

MODULE 6: MANAGING STAKEHOLDER, COMMUNICATION, RESOURCE AND PROCUREMENT MANAGEMENT

- Project Stakeholder Management: Chapter 13 (pp. 505–526)
- Project Communication Management: Chapter 10 (pp. 359–376)
- Project Resource Management: Chapter 9 (pp. 307–358)
- Project Procurement Management: Chapter 12 (pp. 467–504)

1. KENAPA PENTING EMPAT ASPEK INI DALAM PENGURUSAN PROJEK?

Stakeholder, Communication, Resource dan Procurement merupakan 4 “enablers” utama kejayaan sesuatu projek.

Penjelasan:

- **Stakeholders:** Mereka yang mempunyai pengaruh atau kepentingan terhadap projek (p. 506)
- **Communication:** 90% masa seorang pengurus projek digunakan untuk berkomunikasi (p. 360)
- **Resources:** Tiada projek berjaya tanpa manusia dan bahan (p. 309)
- **Procurement:** Banyak projek bergantung kepada vendor, kontraktor, dan pembelian luaran (p. 468)

Tips Pelaksanaan:

Gunakan Stakeholder Register, Resource Histogram, dan Communication Matrix untuk merancang dan menyelaraskan aktiviti.

2. CABARAN PENGURUSAN STAKEHOLDER DI MALAYSIA

Realiti Semasa:

- Pegawai atasan kurang terlibat atau sering tukar arahan.
- Projek awam sukar dapat “buy-in” komuniti.
- Politiking organisasi dan konflik minat.

Penyelesaian:

- **Power/Interest Grid:** Kenal pasti siapa perlu diutamakan.
- **Early Engagement:** Libatkan stakeholder sejak peringkat inisiasi.
- **One-to-One Influence:** Bina kepercayaan secara personal dan bukan hanya formaliti.

Maklum Balas Berkaitan:

“Saya mahu tahu bagaimana menguruskan orang atasan dengan baik.”

3. CARA MENGURUS "SUPERIOR" & "CUSTOMER NOT A KING"

Isu:

- Bos yang banyak beri arahan tetapi tidak beri masa/sumber.
- Pelanggan yang menganggap projek mesti ikut kehendak mereka tanpa memahami batasan.

Strategi:

- Gunakan Issue Log & Escalation Path dari PMBOK.
- Amalkan assertive communication: Tegas tetapi hormat.
- Terapkan mutual expectation melalui project charter dan perjanjian awal.

4. CABARAN PENGURUSAN KOMUNIKASI

Isu Semasa di Malaysia:

- Jurang generasi (Gen Z vs Gen X)
- Kebergantungan berlebihan pada WhatsApp
- Tiada "formal communication plan"

Penyelesaian:

- Gunakan Communication Management Plan (p. 362)
- Latih pasukan menggunakan sistem rasmi seperti Teams / Trello / Slack
- Ajar komunikasi dua hala — bukan hanya arahan sehalu.

Aktiviti Ringkas (5 min):

Simulasi komunikasi antara Project Manager, vendor dan team dalam situasi salah faham.

5. CABARAN PENGURUSAN SUMBER (PEOPLE & MATERIAL)

Realiti:

- Staf multi-projek, keletihan & demotivasi.
- Kekurangan sumber mahir (skilled manpower gap).
- Tugas berganda tanpa kejelasan peranan.

Strategi:

- Gunakan **Responsibility Assignment Matrix (RAM)** dan **RACI Chart** (p. 318)
- Bina **Team Charter** dan perelaskan ekspektasi.
- Jalankan sesi motivasi & **team building** berkala.

Maklum Balas Berkaitan:

"Saya dapat motivasi untuk bantu staf cari jalan penyelesaian."

6. CABARAN PENGURUSAN PROCUREMENT

Isu Terkini:

- Tender lambat, prosedur berat, dan vendor tidak kompeten.
- Ketidaktelusan atau monopoli vendor.
- Harga naik selepas projek bermula.

Strategi:

- Rancang melalui **Procurement Management Plan** (p. 471)
- Gunakan **multi-vendor strategy** untuk kurangkan risiko tunggal.
- Audit vendor secara berkala dan nilai prestasi mereka dengan metrik (KPI Vendor).

Contoh di Malaysia:

Projek kerajaan mengalami kelewatan disebabkan vendor tidak membekal tepat masa — mitigasi dengan **Performance-Based Contracts**.

PENUTUP & AKTIVITI PENILAIAN DIRI (10 MIN)

- Gunakan soalan refleksi seperti:
 - Siapa stakeholder saya yang paling kritikal minggu ini?
 - Apakah bentuk komunikasi saya gunakan? Berkesan atau tidak?
 - Apa satu tindakan kecil saya boleh ambil untuk bantu team saya minggu ini?
- Lakukan **kuiz cepat (5 soalan MCQ)** melalui Google Form atau Kahoot.

✓ Kesimpulan Modul

- Semua komponen dalam modul ini **berkait secara langsung dengan kejayaan penyampaian projek (project delivery)**.
- Menjawab maklum balas seperti "mahu tahu cara pengurusan yang efisien" dan "nak urus projek dengan teratur".
- Memberi pendedahan sebenar, praktikal dan mudah difahami walaupun oleh peserta bukan berlatar belakang teknikal.



RISK AND QUALITY MANAGEMENT



DMY Khairulanwar Misnan



Muslim Professional Helpers Center

Challenge

- Use and update Risk Register
- Conduct risk workshops
- Build risk awareness culture
- Use risk management tools (Primavera, MS Project)
- Apply lessons from past projects
- Implement QA & QC continuously
- Regular internal audits and spot checks
- Define clear quality criteria
- Build a quality-focused team culture
- Engage external auditors or experts

MODULE 7: RISK AND QUALITY MANAGEMENT

- Project Risk Management: Chapter 11 (pp. 395–446)
- Project Quality Management: Chapter 8 (pp. 271–306)

1. APAKAH KEPENTINGAN MENGURUSKAN RISK DAN QUALITY?

Risk Management penting untuk mengenal pasti potensi masalah sebelum ia berlaku dan menyediakan pelan mitigasi untuk mengurangkan impaknya terhadap objektif projek.

Quality Management pula memastikan hasil projek memenuhi keperluan pelanggan dan standard organisasi, meningkatkan reputasi serta mengurangkan pembaziran dan kerja semula.

2. APAKAH CABARAN YANG BIASANYA BERLAKU DALAM PENGURUSAN RISIKO MENGIKUT KEADAAN SEMASA DI MALAYSIA?

- Ketidakpastian ekonomi & polisi kerajaan – perubahan bajet, polisi cukai, peralihan kerajaan.
- Risiko cuaca & bencana alam – banjir dan cuaca ekstrem sering menjejaskan projek infrastruktur.
- Ketidakpastian rantai bekalan (supply chain) – isu geopolitik dan kebergantungan pada sumber luar.
- Kurangnya budaya pengurusan risiko proaktif – organisasi hanya bertindak selepas risiko berlaku.

3. BAGAIMANA CARA MENANGANI ISU DAN CABARAN YANG BERLAKU DALAM PENGURUSAN RISIKO MENGIKUT KEADAAN SEMASA DI MALAYSIA?

- Gunakan Risk Register awal dan kemas kini berkala.
- Adakan sesi risk workshop melibatkan semua stakeholder.
- Bina budaya 'risk-aware' – latih pasukan agar sentiasa mengesan, melaporkan dan menilai risiko.
- Gunakan software pengurusan risiko seperti Primavera Risk Analysis atau MS Project Risk.
- Gunakan Lessons Learned daripada projek terdahulu.

4. APAKAH CABARAN YANG BIASANYA BERLAKU DALAM PENGURUSAN KUALITI MENGIKUT KEADAAN SEMASA DI MALAYSIA?

- Tiada Standard Operating Procedures (SOP) yang dikemaskini atau tidak dipatuhi.
- Tekanan untuk menyiapkan projek dengan cepat menyebabkan kompromi terhadap kualiti.
- Kurangnya latihan dan kesedaran tentang kualiti dalam kalangan pasukan pelaksana.
- Kualiti vendor/sub-kontraktor tidak konsisten – isu biasa dalam projek kerajaan dan swasta.

5. BAGAIMANA CARA MENANGANI ISU DAN CABARAN YANG BERLAKU DALAM PENGURUSAN KUALITI MENGIKUT KEADAAN SEMASA DI MALAYSIA?

- Laksanakan Quality Assurance (QA) dan Quality Control (QC) secara berterusan.
- Audit dalaman berkala dan 'spot-check' ke atas deliverables.
- Tentukan kriteria kualiti dengan jelas dalam dokumen projek.
- Bina 'Quality Culture' dalam pasukan projek, bukan sekadar fokus pada hasil akhir.
- Libatkan pakar kualiti atau juruaudit luar secara berkala.

6. BAGAIMANA INTEGRATION MANAGEMENT BERFUNGSI DALAM MENGURUSKAN KESEMUA KNOWLEDGE AREA OF PROJECT MANAGEMENT?

Integration Management bertindak sebagai 'pengikat utama' yang menyatukan kesemua 10 Knowledge Areas dalam PMBOK, iaitu:

- Scope, Schedule, Cost, Quality, Resource, Communication, Risk, Procurement, Stakeholder & Integration.

Ia memastikan semua proses selari dengan objektif projek melalui:

- **Develop Project Charter & Project Management Plan**
- **Direct and Manage Project Work**
- **Monitor and Control Project Work**
- **Perform Integrated Change Control**
- **Close Project or Phase**
